

Lab 2: Agile Backlog Creation & Sprint Simulation in Jira

Student Project Portfolio & Showcase App

Submitted by: Mohammed Shahid Javed Mokashi | Jira Project: SE LAB (SCRUM)

SRN:PES1UG24AM378

1. Epics

Three Epics were created in Jira, derived from the functional requirements in the Lab 1 problem statement (Student Project Portfolio & Showcase App).

Epic 1 (SCRUM-5): Team Showcase Profile Management

Enable student teams to create and publish project profiles with abstract summaries, demo video links, and verified GitHub repository URLs. | Priority: High

Epic 2 (SCRUM-6): Judge Evaluation & Digital Rubrics

Enable panel judges to view assigned projects and score them using structured digital rubrics. | Priority: High

Epic 3 (SCRUM-7): Public Voting & Anti-Sybil Protection

Enable the public to vote on showcased projects with safeguards against fraudulent voting, plus a real-time leaderboard. | Priority: Medium

Backlog: Epics & User Stories (Jira Screenshot)

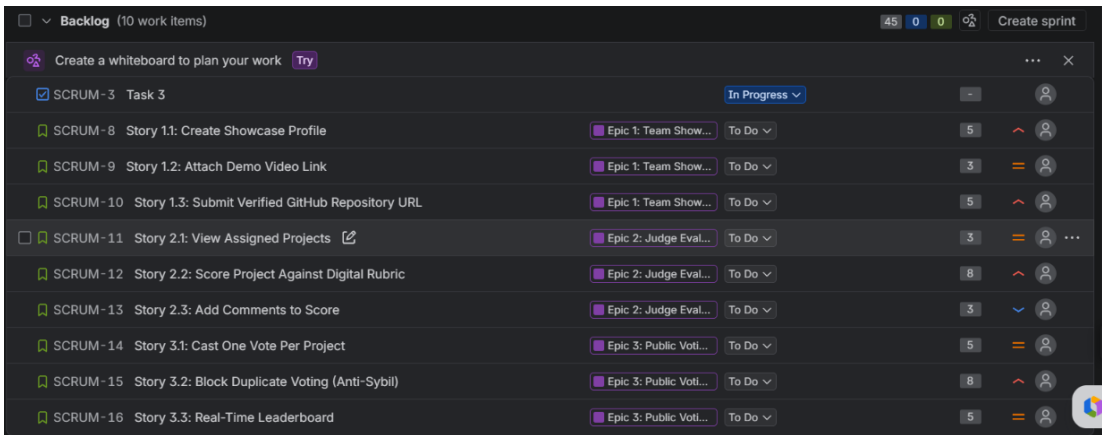


Figure 1 — Jira Backlog showing all 3 Epics with their linked User Stories, priorities, and story points.

2. User Stories & Story Point Estimation

Story points were assigned using the Fibonacci scale (3, 5, 8) based on complexity, effort, and uncertainty.

Epic 1: Team Showcase Profile Management

Key	Story	Priority	Points
SCRUM-8	As a student team, I want to create a showcase profile with an abstract summary, so that judges and the public understand our project.	High	5

Key	Story	Priority	Points
SCRUM-9	As a student team, I want to attach a demo video link to my profile, so that viewers can see the project in action.	Medium	3
SCRUM-10	As a student team, I want to submit a verified GitHub repository URL, so that my code is accessible and validated before publishing.	High	5

Epic 2: Judge Evaluation & Digital Rubrics

Key	Story	Priority	Points
SCRUM-11	As a panel judge, I want to view a list of assigned projects, so that I know what to evaluate.	Medium	3
SCRUM-12	As a panel judge, I want to score a project against a digital rubric, so that grading is consistent and structured.	High	8
SCRUM-13	As a panel judge, I want to add comments to my score, so that I can justify my evaluation.	Low	3

Epic 3: Public Voting & Anti-Sybil Protection

Key	Story	Priority	Points
SCRUM-14	As a public visitor, I want to cast one vote per project, so that voting reflects genuine popularity.	Medium	5
SCRUM-15	As a public visitor, I want to be blocked from voting multiple times (device/IP/OTP checks), so that the leaderboard isn't manipulated.	High	8
SCRUM-16	As a public visitor, I want to see a real-time leaderboard, so that I can track which projects are trending.	Medium	5

3. Sprint Simulation

SCRUM Sprint 1 was created with a 1-week duration (Sep 1 – Sep 15, 2026) and populated with backlog items including the new User Stories.

Sprint Board — Initial State (Sprint Started)

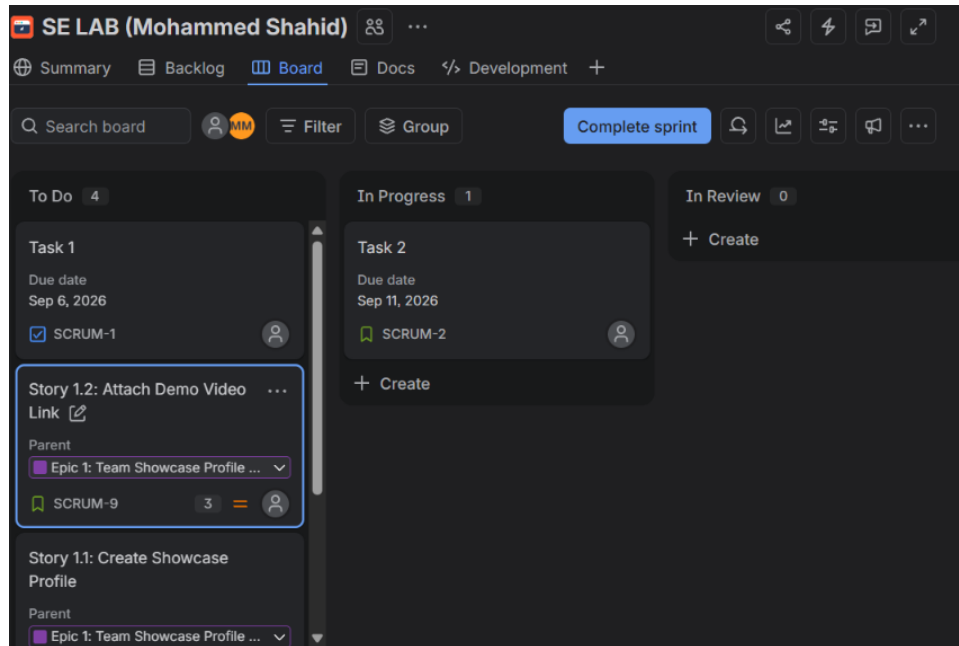


Figure 2 — Active Sprint board immediately after Start Sprint, with items in To Do and In Progress.

Sprint Board — Progressing Tasks (To Do → In Progress → Done)

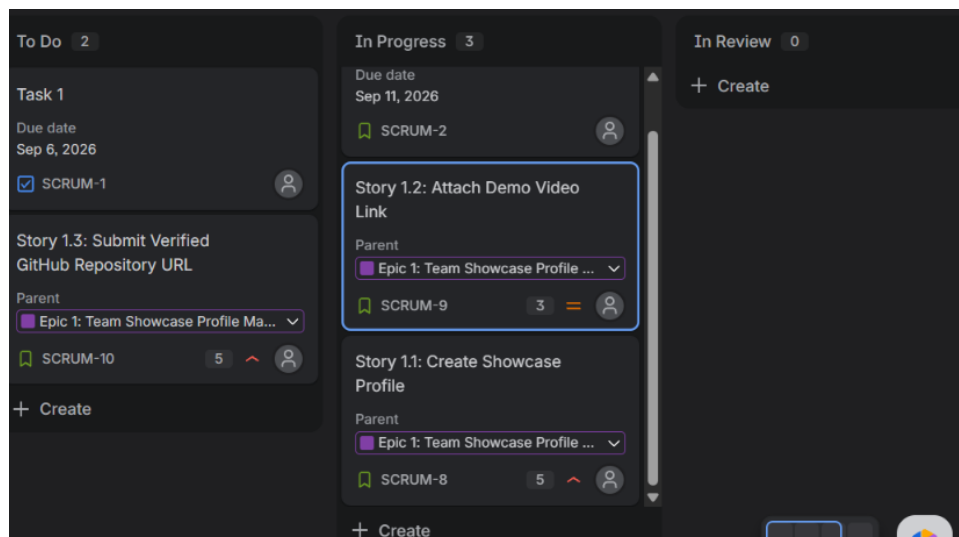


Figure 3 — Stories 1.1 and 1.2 moved into In Progress (later marked Done, reflected in the burndown chart below) while Story 1.3 remains in To Do, simulating real sprint progress.

4. Burndown Chart

The Burndown Chart (Reports → Burndown Chart) tracks remaining story points against the ideal guideline over the sprint duration.

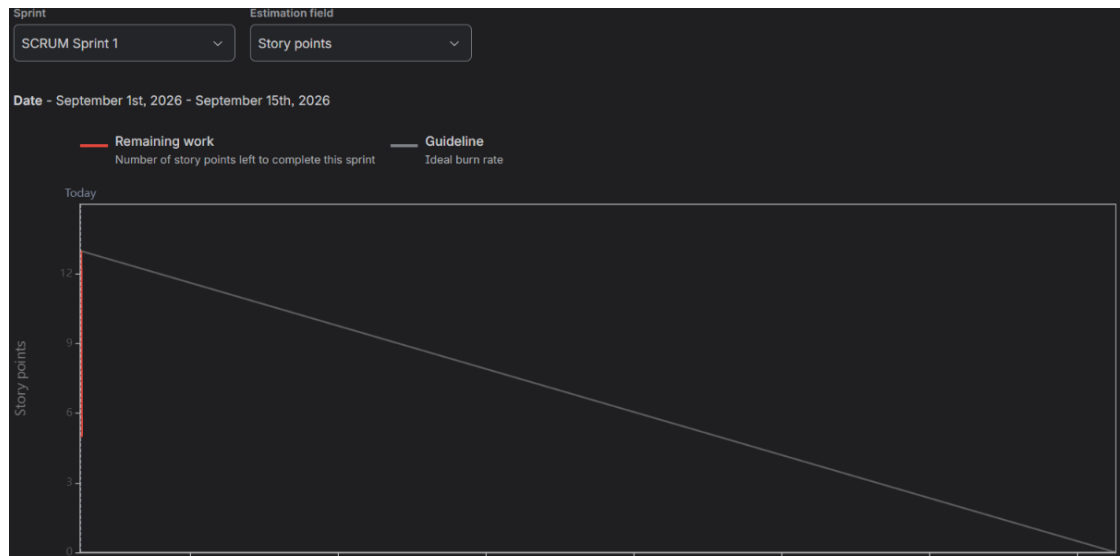


Figure 4 — Sprint burndown showing remaining work dropping from 13 points as Stories 1.1 (5 pts) and 1.2 (3 pts) were completed, against the ideal guideline line.

5. Reflection Questions

1. Did your estimations reflect the actual effort?

The Fibonacci-based estimates (3, 5, 8) captured relative complexity reasonably well. Simpler CRUD-style stories such as viewing assigned projects (3 pts) were estimated lower than stories with more moving parts, like the digital rubric scoring flow (8 pts) or anti-sybil voting protection (8 pts), which involve validation logic and edge cases. In a real team setting, planning poker with multiple estimators would likely refine these numbers further, especially for the higher-uncertainty items.

2. Was your backlog well-prioritized?

Yes — profile creation and repository verification (Epic 1) were marked High priority since they are prerequisites for judges to evaluate anything at all. Judge scoring (Epic 2) was also High priority given it's core to the grading workflow, while voting features (Epic 3) were set to Medium/Low where they are enhancements rather than blockers. This reflects a logical dependency order: teams must submit before judges can score, and judging can happen independently of public voting.

3. How did your simulated sprint align with your plan?

Sprint 1 planned to complete the three Team Showcase Profile stories (13 points total). Two of the three (Stories 1.1 and 1.2, 8 points combined) were moved to Done during the simulation, while Story 1.3 remained in To Do. This is a realistic outcome — teams often carry over 1-2 items to the next sprint rather than completing 100% of planned scope, especially when uncertainty exists in later stories.

4. What insights did the burndown chart give about your team's capacity?

The chart's remaining-work line dropped below the ideal guideline early (as two stories were completed close together), then flattened — indicating the last story wasn't finished within the visible window. This pattern suggests capacity was front-loaded: quick wins were completed first, and the more complex/dependent item (GitHub repo verification) was left for later. It signals that future sprints should either break down large stories further or resequence so effort is spread more evenly across the sprint.
